



सेंद्रल ट्रान्समिशन यटिलिटी ऑफ इंडिया लिमिटेड

(पावर ग्रिड कॉर्पोरेशन ऑफ इंडिया लिमिटेड के स्वामित्व में)

(भारत सरकार का उद्यम)

CENTRAL TRANSMISSION UTILITY OF INDIA LTD.

(A wholly owned subsidiary of Power Grid Corporation of India Limited)

(A Government of India Enterprise)

Ref: CTU/N/00/CMETS_NR/41

Date: 06-11-2025

As per distribution list

Subject: 41st Consultation Meeting for Evolving Transmission Schemes in Northern Region-Minutes of Meeting

Dear Sir/Ma'am,

Please find enclosed the minutes of the 41st Consultation Meeting for Evolving Transmission Schemes in Northern Region held on 10th October 2025 (Friday) through virtual mode.

The minutes are also available at CTU website (www.ctuil.in)

Thanking you,

Yours faithfully,

(R V M M Rao)

Chief General Manager

Distribution List:

Chief Engineer (PSP&A – I) Central Electricity Authority Sewa Bhawan, R.K.Puram, New Delhi-110 066	Member Secretary Northern Regional Power Committee 18A, Shaheed Jeet Singh Sansanwal Marg, Katwaria Sarai, New Delhi – 110 016
Director (Power System) Solar Energy Corporation of India Ltd. D-3, 1 st Floor, A wing, Religare Building, District Centre, Saket, New Delhi-110017	Director Ministry of New and Renewable Energy, Block 14, CGO Complex, Lodhi Road, New Delhi-110003
Director (SO) Grid Controller of India Limited (erstwhile Power System Operation Corporation Ltd.) 9 th Floor, IFCI Towers, 61, Nehru Place, New Delhi-110 016	Executive Director Northern Regional Load Despatch Centre 18-A, Qutab Institutional Area, Shaheed Jeet Singh Sansanwal Marg, Katwaria Sarai, New Delhi– 110 016
Director (P & C) HPPTCL, Headoffice, Himfed Bhawan, Panjari, Shimla-171005 Himachal Pradesh	Director(W&P) UP Power Transmission Company Ltd. Shakti Bhawan Extn, 3rd floor, 14, Ashok Marg, Lucknow-226 001
Director (Technical) Punjab State Transmission Corporation Ltd. Head Office, The Mall, Patiala 147001, Punjab	Director (Projects) Power Transmission Corporation of Uttarakhand Ltd. Vidyut Bhawan, Near ISBT Crossing, Saharanpur Road, Majra, Dehradun.
Development Commissioner (Power) Power Development Department Grid Substation Complex, Janipur, Jammu	Director (Technical) Rajasthan Rajya Vidyut Prasaran Nigam Ltd. Vidyut Bhawan, Jaipur, Rajasthan-302005.
Member (Power) Bhakra Beas Management Board Sector-19 B, Madhya Marg, Chandigarh - 160019	Superintending Engineer (Operation) Electricity Circle, 5 th Floor, UT Secretariat, Sector-9 D, Chandigarh - 161009
Director (Operations) Delhi Transco Ltd. Shakti Sadan, Kotla Road, New Delhi-110 002	Director (Technical) Haryana Vidyut Prasaran Nigam Ltd. Shakti Bhawan, Sector-6, Panchkula-134109, Haryana

Distribution List:

Shri Mithilesh Prasad Dinkar General Manager NHPC Limited NHPC Limited, T&RE Division, Sector-33, Faridabad-121003, Haryana Ph.: 9599500913, 9816605910 Email: trenhpc@nhpc.nic.in ipranjan@nhpc.nic.in	Shri Lalit T. Khanna Chief Operating Officer STT Global Data Centres India Private Limited Plot No 1 Sector 143 Noida UP - 201301. Ph.: 9899707642, 8767524102 Email: lalit.khanna@sttelemediagdc.in ; deepak.chaudhary@sttelemediagdc.in
Shri Shri V. Jayaraman CEO-Power Hindustan Zinc Limited Yashad Bhawan, Udaipur, Rajasthan Ph.: 9928140302, 9799782777 Email: v.jayaraman@vedanta.co.in ; vinod.jaroli@vedanta.co.in	Shri Kamleshkumar Authorized Signatory Panipat Green Hydrogen Private Limited L&T Knowledge City, Gate No. 1, Corporate Block 3rd Floor, NH-8 Ajwa - Waghodia Crossing, Vadodara - 390019 Ph.: 9898127217, 9978969701 Email: kkg@larsentoubro.com jayank.pandya@larsentoubro.com

Minutes of 41st Consultation Meeting for Evolving Transmission Schemes in Northern Region held on 10.10.2025

A. Confirmation of Minutes:

It was informed that, the minutes of 40th CMETS NR meeting held on 12.09.2025 were circulated vide CTU letter dated 30.09.2025. No comments were received by CTUIL regarding the same. Accordingly, minutes of 40th CMETS NR meeting is confirmed as circulated.

It was informed that in view of notification of 3rd Amendment of GNA Regulations, the transition of RE connectivity grantees to Solar & Non-Solar access is under progress. Therefore, application for connectivity for RE projects were not taken up for discussion in the this meeting. However, as there is no impact on processing of GNA/GNA_{RE} applications due to above amendment, the GNA/GNA_{RE} applications were taken up for discussion in this meeting.

A1. Application for grant of GNA_{RE} deferred in the 38th CMETS NR meeting

SI No.	Application No. & Date	Name of the Applicant	Nature of applicant	GNA_{RE} within Region (MW)	GNA_{RE} outside Region (MW)	Total GNA_{RE} Required (MW)	Start date of GNA_{RE}	End date of GNA_{RE}
1.	2200001595 (06-02-2025)	Hindustan Zinc Limited	Bulk consumer seeking to connect to ISTS directly	5.0	215.0	220	30-06-2027	30-06-2052
It was informed that the application for 220 MW GNA_{RE} by Hindustan Zinc Limited(HZL) Debari smelter unit was earlier deliberated in 38th & 39th CMETS NR meetings. HZL Debari smelter plant is currently connected to intra state network at 220kV/132kV Debari GSS of Ajmer Vidyuth Vitran Nigam Limited (AVVNL) in Rajasthan. HZL in the application had informed that they have requested for NOC from AVVNL for disconnection from intra state network. HZL Debari plant is about ~45 km from 765/400 kV Chittorgarh(PG) S/s & about 60 km from 400/220 kV Kankroli S/s. In the 39th CMETS NR meeting, it was informed that, as per the information received from Powergrid, no space is available for additional ICT at Kankroli S/s for augmentation. Further, there is no nearby ISTS S/s with 220 kV switchyard. Accordingly, considering the location of the project after evaluating various options, it was proposed that GNA_{RE} to Hindustan Zinc Ltd. may be granted with ISTS interconnection at 400 kV through LILO of one circuit of Chittorgarh (PG) – Chittorgarh(RVPN) 400 kV D/c line at HZL Debari Switchyard.								

SI No.	Application No. & Date	Name of the Applicant	Nature of applicant	GNA _{RE} within Region (MW)	GNA _{RE} outside Region (MW)	Total GNA _{RE} Required (MW)	Start date of GNA _{RE}	End date of GNA _{RE}
Fig : Loading of Kankroli(PG) ICTs of Past one year (Source: Grid-India) From the loading pattern of Kankroli (PG) ICTs (3x315MVA), it is observed that maximum loading on each 315MVA ICTs is in the range of 230MW-250MW in Summer season. Further in present time frame study file N-1 limit of Kankroli(PG) ICTs is ~230MW/ICT. CTUIL also carried out the studies (in Planning files) for grant of GNA_{RE} to HZL for 220MW as Bulk consumer seeking to connect to ISTS directly . From the studies it is envisaged that , with the commissioning of upcoming 220kV Kankroli(PG)-Nathdwara D/c line & HZL 200MW load (GNA_{RE}) at Kankroli (PG) S/s, loading will increase to 50MW/ICT (under N-1 contingency of 500MVA ICT, expected loading will be 290MW/ICT on 3x315MVA ICT). Further with 220MW HZL Bulk load interconnection at 220kV Kankroli (PG) loading will further increase to 35MW/ICT (under N-1 contingency of 500MVA ICT, expected loading will be 325MW/ICT on 3x315MVA ICTs). As there is no space available for additional ICT at Kankroli S/s, option for interconnection at Kankroli S/s , it was not considered. RVPN in the 39th CMETS NR meeting informed that the studies carried out by CTUIL need to be reviewed considering the proposed Udaipur, Banswara S/s etc. of RVPN and other intra state systems proposed in GEC-III schemes. CTUIL informed that the studies were carried out in 2027-28 timeframe files considering the start date of GNA required by HZL(30 Jun 2027). After deliberations, it was decided that the CTUIL shall carry out studies in both 2027 & 2030 timeframe (with GEC-III schemes) and share the study files with RVPN & Grid India. Subsequently, further studies were carried out for grant of GNA_{RE} to HZL(Debari). Based on the revised studies carried out by CTUIL, following options were proposed to grant GNA_{RE} to HZL: Option:1: Through LILO of one circuit of 400 kV Chittorgarh(PG) – Chittorgarh(RVPN) D/c line It was informed that this option was already proposed in the 39th CMETS NR meeting held on 28.07.2025. The same option was studied in the revised study file with updated Rajasthan system. In this proposal, GNA_{RE} to Hindustan Zinc Limited can be grated with ISTS interconnection at 400 kV through LILO of one circuit of Chittorgarh (PG) – Chittorgarh(RVPN) 400 kV D/c line at HZL Debari Switchyard								

SI No.	Application No. & Date	Name of the Applicant	Nature of applicant	GNA _{RE} within Region (MW)	GNA _{RE} outside Region (MW)	Total GNA _{RE} Required (MW)	Start date of GNA _{RE}	End date of GNA _{RE}
			LILO length of proposed Chittorgarh(PG) – Chittorgarh(RVPN) line at Debari is about 50 km. In this regard, it may be noted that the Chittorgarh(PG) – Chittorgarh(RVPN) line is a Quad Moose line. Therefore, the LILO portion should also be implemented using the Quad Moose conductor by the licensee or M/s HZL itself as applicable. Further, HZL shall also implement 400kv line bays at their generation switchyard commensurate to line capacity (Quad configuration) From the studies, it is observed that with the LILO arrangement, the power flow is in order in base case as well as N-1 contingency scenarios. Further, this LILO arrangement shall also relieve the loading of 400/220 kV ICTs at Chittorgarh (RVPN) S/s which is currently N-1 non-compliant. Option:2: <u>Through LILO of one circuit of 400 kV Sirohi – Chittorgarh(PG) D/c line:</u> The second option proposed was through LILO of one circuit of Sirohi – Chittorgarh(PG) 400 kV D/c line at HZL Debari Switchyard. Sirohi – Chittorgarh (PG) 400 kV D/c line which is currently under construction as part of Transmission system for evacuation of power from Rajasthan (Jaisalmer/Barmer Complex) (Ph-IV Part-2:5.5 GW) with the scheduled commissioning date of 31.12.2026 (Anticipated COD). Considering the start date of GNA_{RE} requested by HZL(Jun'27), it was proposed to grant GNA_{RE} to Hindustan Zinc Limited with ISTS interconnection at 400 kV through LILO of one circuit of Sirohi – Chittorgarh(PG) 400 kV D/c line at HZL Debari Switchyard LILO length of proposed Sirohi – Chittorgarh(PG) line at Debari is about 25 km. In this regard, it was mentioned that the Sirohi – Chittorgarh(PG) line is a Quad Moose line. Therefore, the LILO portion should also be implemented using the Quad Moose conductor by the licensee or M/s HZL itself as applicable. Further, HZL shall also implement 400kV line bays at their generation switchyard commensurate to line capacity (Quad configuration). HZL noted and agreed for the same. Details of studies are enclosed in Exhibit-II. From the studies, it is observed that with the LILO arrangement, the power flow is in order in base case as well as N-1 contingency scenarios. <u>Deliberations in 41st CMETS NR meeting:</u> RVPN in the meeting informed that LILO of one circuit of 400 kV Chittorgarh(PG)-Chittorgarh(RVPN) line(Option-1) leads to increase in loading of other circuit of 400 kV Chittorgarh(PG)-Chittorgarh(RVPN) line. As per the study, it is about 850 MW. Further, considering the expected future load growth in Chittorgarh area, the loading may increase. However in case of LILO of Sirohi-Chittorgarh D/c line the difference in loading is not significant. Further, the LILO length is also less in case of Sirohi Chittorgarh option. Therefore, RVPN recommended to consider option-2 for grant of GNA_{RE} to HZL. Grid India in the meeting informed that LILO of Quad moose line for 200 MW GNA_{RE} leads to under utilization of line capacity and therefore requested CTUIL to explore any other option. Regarding this, CTUIL clarified that as already informed, there is no nearby ISTS substation with 220 KV switchyard except Kankroli where there is no margin due to limitation of space for additional ICT. Therefore, considering the above, the feasible options(both Option1 & Option2) were proposed by CTUIL.					

SI No.	Application No. & Date	Name of the Applicant	Nature of applicant	GNA _{RE} within Region (MW)	GNA _{RE} outside Region (MW)	Total GNA _{RE} Required (MW)	Start date of GNA _{RE}	End date of GNA _{RE}
CTUIL suggested that for optimal utilization of ISTS line, HZL shall keep space for minimum 2 no. of 220 kV bays at their switchyard so that in case of any additional load requirement arises in future either by HZL itself or any other drawl entity, the connectivity can be provided through the switchyard utilising the same LILO line. HZL agreed for the same. After deliberation on both options, it was agreed to grant GNA_{RE} to HZL with LILO of one circuit of 400 kV Sirohi-Chittorgarh D/c line at HZL Switchyard(Option-2). Further, Details of transmission system for Grant of GNA_{RE} is as below: <u>Details of Transmission System for Grant of GNA_{RE}:</u> A. Dedicated Transmission system for GNA_{RE} (to be constructed and maintained by HZL or by an ISTS licensee at the cost of HZL): (i) LILO of one circuit of 400 kV Sirohi – Chittorgarh(PG) D/c line(Quad) at Hindustan Zinc(Debari) Switchyard along with 2 nos. 400kV line bays at Hindustan Zinc(Debari) Switchyard(with capacity commensurate to Quad moose line capacity) B. Common Transmission system for GNA_{RE} (under ISTS): (i). Establishment of 765/400 kV Sirohi S/s(under construction) (ii). Sirohi- Chittorgarh(PG) 400 kV D/c line (under construction) (one ckt is proposed to be LILOed at M/s HZL switchyard) (iii). Existing system beyond 765/400 kV Chittorgarh (PG) S/s Start date of GNA_{RE}: 30.06.2027 (subject to availability of common transmission system as indicated above) End date of GNA_{RE}: 30.06.2052 Further, it was highlighted that, there is no provision for dual connectivity (both STU & ISTS) to Bulk consumer under Connectivity & GNA Regulations 2022. As HZL Debari plant is presently connected with STU network of RVPN and seeking direct connectivity to ISTS, it is necessary to submit NoC from STU for disconnection from intra state network. Accordingly, M/s HZL may expedite submission of NOC from RVPN for disconnection. Intimation for grant of GNA_{RE} shall be issued by CTUIL only upon submission of NoC from STU for disconnection. HZL & RVPN may update regarding the NoC. As per 22.2(b-i) of GNA Regulations 2022, Conn BGs are required to be submitted by HZL within one month of issuance of intimation by CTUIL as below: • Conn BG-1: Rs. 50 lakh • Conn BG-3: Rs. 2 lakh/MW M/s Hindustan Zinc Ltd. noted and agreed for the same.								

Minutes of 41st Consultation Meeting for Evolving Transmission Schemes in Northern Region held on 10.10.2025

SI No.	Application No. & Date	Name of the Applicant	Nature of applicant	GNA _{RE} within Region (MW)	GNA _{RE} outside Region (MW)	Total GNA _{RE} Required (MW)	Start date of GNA _{RE}	End date of GNA _{RE}
2.	2200002025 (17.05.2025)	Hindustan Zinc Limited	Bulk consumer seeking to connect to ISTS directly	5	175	180	01.02.2027	31.01.2052

The above application for GNA_{RE} of 180 MW by Hindustan Zinc for their Rampur Agucha Mining Facility in Bhilwara district, Rajasthan was deliberated in the 39th CMETS NR meeting held on 28.07.2025. In the 39th CMETS NR meeting, NRLDC informed that due to high loading of 400kV Anta-Kota line, 400kV Anta-Chhabra and 400kV Anta-Kota line is bypassed at Anta and the lines are in service as 400kV Chhabra-Kota line (bypassed at 400kV Anta) as agreed in 154th OCC meeting of NRPC held on 18.12.2018. Further, during solar hours 400 kV Bikaner(RVPN) – Merta line is also heavily loaded. Therefore, the detailed studies need to be carried out before granting this application through LILO of Shree Cement. Accordingly, it was decided that the above application shall be discussed in the next CMETS NR meeting further studies.

Subsequently, considering the location of the project, various options were explored to identify the system for interconnection of HZL Rampur-Agoocha and grant of GNA_{RE} of 180 MW. For the capacity of 180 MW, interconnection at any S/s at 220 kV level is the optimal solution. However, it is observed that there is no nearby ISTS substation with existing 220 kV system. The nearest existing ISTS S/s with 220 kV switchyard is Kankroli which is at a distance of 135 km from the project which is very distant. Further, as informed earlier during discussion of HZL application at Debari, there is space constraint at Kankroli(PG) S/s for augmentation of ICT capacity. Accordingly, after evaluating various options, it was proposed to grant GNA_{RE} with LILO of 400 kV Shree Cement- Kota line at HZL Rampur- Agoocha switchyard as proposed earlier in the 39th CMETS NR meeting. The GNA_{RE} of 180 MW can be granted through LILO of 400 kV Shree Cement – Kota line at HZL switchyard. The LILO length shall be about 25 km. Details of studies are enclosed in **Exhibit-III**.

From the studies, it is observed that with the LILO arrangement, the power flow is in order in base case as well as N-1 contingency scenarios. Further, studies were also carried out in the present scenario file of Grdi India and it was also observed that the loading of Bypassed Chhabra-Anta-Kota line is about 780 MW. With additional load of HZL the loading increases to around 820 MW. However, with the commissioning of Beawar S/s, the loading of Chhabra-Anta-Kota line reduces back to 780 MW.

Deliberations in 41st CMETS NR meeting:

Grid India in the meeting informed that the loading of Chhabra-Anta Kota remains high during non solar hours when thermal generations peak. Therefore, granting GNA to HZL with Kota-Shree cement LILO shall further increase the loading of the line. Further, RVPN is planning Anta-2 transmission system for evacuation of additional Thermal generation projects in Anta-Chhabra area. Therefore, if the loading of Chhabra Anta -Kota is relieved with Anta-2 transmission system and the timeline of HZL project and Anta-2 system matches then GNA may be granted to HZL matching with Anta-2 transmission system.

Regarding this, RVPN clarified that Anta-2 system is yet to be awarded and considering the implementation schedule of 30 months from the date of award, it may take minimum 3.5 to 4 years from the present date for commissioning of Anta-2 system. RVPN suggested that, HZL may take up the reconductoring of RVPNs 400kV Chhabra-Anta-Kota line under their scope matching with their start date so that the GNA_{RE} can be granted with the proposed LILO of 400 kV Kota-Shree Cement

Minutes of 41st Consultation Meeting for Evolving Transmission Schemes in Northern Region held on 10.10.2025

SI No.	Application No. & Date	Name of the Applicant	Nature of applicant	GNA _{RE} within Region (MW)	GNA _{RE} outside Region (MW)	Total GNA _{RE} Required (MW)	Start date of GNA _{RE}	End date of GNA _{RE}
line. Regarding this, HZL informed that reconductoring of line is not feasible as they face difficulty in getting permission for shut down of line which are heavily loaded within the limited time period they have for start date of GNA_{RE}. CTUIL informed that the GNA start date requested by HZL is Feb'27, therefore grant of GNA_{RE} to HZL with Anta-2 transmission system is not feasible. However, HZL may explore the possibility of reconductoring as suggested by RVPN. Alternatively, CTU suggested other feasible option for interconnection i.e. 765/400 kV Beawar substation at 220 kV level. In Beawar S/s, space for 220 kV system is kept as part of future provisions. Therefore, if HZL agrees for grant at Beawar S/s, then as per 12.5 of GNA Regulations, the dedicated 220 kV D/c line to connect HZL to Beawar S/s & Augmentation of 2x500 MVA 400/220kV ICTs at Beawar S/s is to be constructed & maintained by HZL or by a ISTS licensee at the cost of M/s HZL. HZL noted the same. HZL informed that they shall assess the option of interconnection at 220kv level of Beawar S/s and confirm in one week's time. Accordingly, based on the request of M/s HZL it was decided to take up the above application for grant at Beawar in next CMETS-NR meeting. CTUIL informed that there is no option to change the start date of GNA_{RE}. Therefore, HZL may inform their decision as early as possible so that the grant may be finalised in the next meeting. HZL agreed for the same. Further, it was informed that there is no provision for dual connectivity (both STU & ISTS) to Bulk consumer under Connectivity & GNA Regulations 2022. As HZL Debari plant is presently connected with STU network of RVPN and seeking direct connectivity to ISTS, it is necessary to submit NoC from STU for disconnection from intra state network. Accordingly, M/s HZL may expedite submission of NOC from RVPN for disconnection. Intimation for grant of GNA_{RE} shall be issued by CTUIL only upon submission of NoC from STU for disconnection. HZL noted and agreed for the same.								

A2. Application for grant of GNA_{RE} received in Jun'25

SI No.	Application No. & Date	Name of the Applicant	Nature of applicant	GNA _{RE} within Region (MW)	GNA _{RE} outside Region (MW)	Total GNA _{RE} Required (MW)	Start date of GNA _{RE}	End date of GNA _{RE}
1.	2200002213 (30.06.2025)	STT Global Data Centres India Private Limited	Drawee entity connected to Intra State	0	2	2	01.07.2025	30.04.2050
2.	2200002215 (30.06.2025)	STT Global Data Centres India Private Limited	Drawee entity connected to Intra State	0	7	7	01.07.2025	31.03.2035

SI No.	Application No. & Date	Name of the Applicant	Nature of applicant	GNA _{RE} within Region (MW)	GNA _{RE} outside Region (MW)	Total GNA _{RE} Required (MW)	Start date of GNA _{RE}	End date of GNA _{RE}
1.	2200002213 (30.06.2025)	STT Global Data Centres India Private Limited	Drawee entity connected to Intra State	0	2	2	01.07.2025	30.04.2050

Minutes of 41st Consultation Meeting for Evolving Transmission Schemes in Northern Region held on 10.10.2025

SI No.	Application No. & Date	Name of the Applicant	Nature of applicant	GNA _{RE} within Region (MW)	GNA _{RE} outside Region (MW)	Total GNA _{RE} Required (MW)	Start date of GNA _{RE}	End date of GNA _{RE}
It was informed that M/s STT Global Data Centres India Private Limited has applied for GNA_{RE} of 2 MW (Outside the region) as a drawee entity connected to Intra State Transmission System of Uttar Pradesh(UPPTCL) at 33kV level of 400/220/33 kV Sector 148 S/s & 220/33 kV Sector 129 S/s. M/s STT Global Data Centres India Private Limited has also submitted necessary NoC from UPPTCL(STU) for grant of GNA_{RE} of 2 MW in this regard. Accordingly, it was proposed to grant 2 MW of GNA_{RE} (outside the region) to STT Global Data Centres India Private Limited. NRLDC and UPPTCL provide their views on proposal. It was highlighted that M/s STT Global Data Centres India Private Limited has applied for GNA_{RE} vide application dated 30.06.2025 and the start date of GNA_{RE} requested in the application is the immediate next day of application i.e. 01.07.2025. CTUIL informed the applicant that processing of application involves scrutiny of applications followed by system studies, issuance of agenda, discussion in CMETS NR meeting, issuance of minutes of meeting & intimation etc. Therefore, applicants were requested to ensure that sufficient time is available between application date & start date of GNA_{RE} (preferably minimum 3 months) so that CTUIL can process their application and issue intimation for grant in timely manner. M/s STT Global noted the same. Further, it was informed that , the Start date of GNA_{RE} requested by M/s STT Global has already passed & there is no provision to change the start date under GNA Regulations. However, as the GNA_{RE} is being granted through existing system & no augmentation is required, the intimation for grant of GNA_{RE} shall be issued as early as possible & the GNA_{RE} shall be made effective from two days post the intimation date accordingly. M/s STT Global in the meeting informed that they had a change of plan and wish to withdraw the above application. Subsequently, M/s STT Global vide mail dated 10.10.2025 confirmed their decision for withdrawal of the above application. Accordingly, it was decided to close the above application.								

SI No.	Application No. & Date	Name of the Applicant	Nature of applicant	GNA _{RE} within Region (MW)	GNA _{RE} outside Region (MW)	Total GNA _{RE} Required (MW)	Start date of GNA _{RE}	End date of GNA _{RE}
2.	2200002215 (30.06.2025)	STT Global Data Centres India Private Limited	Drawee entity connected to Intra State	0	7	7	01.07.2025	31.03.2035
It was informed that M/s STT Global Data Centres India Private Limited has applied for GNA_{RE} of 7 MW (Outside the region) as a drawee entity connected to Intra State Transmission System of Delhi(DTL) at 33 kV Masjid Mod & 33 kV VSNL S/s of BRPL. M/s STT Global Data Centres India Private Limited has also submitted necessary NoC from DTL(STU) for grant of GNA_{RE} in this regard. Accordingly, it was proposed to grant 7 MW of GNA_{RE} (outside the region) to STT Global Data Centres India Private Limited. NRLDC and DTL provide their views on proposal. It was highlighted that M/s STT Global Data Centres India Private Limited has applied for GNA_{RE} vide application dated 30.06.2025 and the start date of GNA_{RE} requested in the application is the immediate next day of application i.e. 01.07.2025. CTUIL informed the applicant that processing of application involves scrutiny of applications followed by system studies, issuance of agenda, discussion in CMETS NR meeting, issuance of minutes of meeting & intimation etc. Therefore, applicants were requested to ensure that sufficient time is available between application date & start date of GNA_{RE} (preferably minimum 3 months) so that CTUIL can process their application and issue intimation for grant in timely manner. M/s STT Global noted the same. Further, it was informed that, the Start date of GNA_{RE} requested by M/s STT Global has already passed & there is no provision to change the start date under GNA Regulations. However, as the GNA_{RE} is being granted through existing system & no augmentation is required, the intimation for grant of GNA_{RE} shall be issued as early as possible & the GNA_{RE} shall be made effective from two days post the intimation date accordingly.								

SI No.	Application No. & Date	Name of the Applicant	Nature of applicant	GNA _{RE} within Region (MW)	GNA _{RE} outside Region (MW)	Total GNA _{RE} Required (MW)	Start date of GNA _{RE}	End date of GNA _{RE}
M/s STT Global in the meeting informed that they wish to revise the start date of GNA _{RE} to Jan 26. Regarding this, CTUIL clarified that as already informed there is no provision in regulations to change the start date. M/s STT Global informed that they wish to withdraw the above application. Subsequently, M/s STT Global vide mail dated 10.10.2025 confirmed their decision for withdrawal of the above application. Accordingly, it was decided to close the above application.								

A3. Application for grant of GNA_{RE} received in July'25

SI No.	Application No. & Date	Name of the Applicant	Nature of applicant	GNA _{RE} within Region (MW)	GNA _{RE} outside Region (MW)	Total GNA _{RE} Required (MW)	Start date of GNA _{RE}	End date of GNA _{RE}
1	2200002261 (17.07.2025)	Panipat Green Hydrogen Private Limited	Bulk consumer (including Green Hydrogen / Green Ammonia) seeking to connect to ISTS directly	0	99	99	25.08.2027	25.12.2052
It was informed that Panipat Green Hydrogen Pvt. Ltd. (PGHPL) has applied for GNA_{RE} of 99 MW with proposed ISTS interconnection at 400/220 kV Jind(PG) S/s at 220 kV. Powergrid has confirmed the availability of 220 kV bays (2 no.) at Jind(PG) S/s. It was mentioned that, at present, the total transformation capacity available at Jind (PG) S/s is of 1500 MVA(3x500 MVA ICTs). The critical loading of Jind(PG) ICTs(3x500 MVA) under N-1 with existing & proposed interconnections of HVPNL & transmission system for Bikaner-IV PS was already highlighted by CTUIL in the 27th CMETS NR meeting held on 10.01.2024 under discussions related to Bikaner-IV transmission scheme. In the 27th CMETS NR meeting, Grid-India had stated that as the present loading on 2x500MVA ICT is about 500MW (peak), the ICT augmentation(4th) at Jind(PG) S/s may be considered at later stage after commissioning of upcoming HVPNL interconnections & 400/220kV ICT (3rd) at Jind(PG). HVPNL in the same meeting had stated that 400kV Munakh S/s for power evacuation of YTPP (800MW) is under planning. Additionally, 640MVA load will be envisaged progressively from 2027 by IOCL. Accordingly, requirements will be assessed based on Grid-India operational feedback report and loading diversion in planning studies considering HVPNL proposal for evacuation of power from YTPP generation (800MW). From the studies, it is observed that the incremental loading of ICTs due to Bulk Consumer load shall further increase to about 15 MW/ICT. Based on application of 99 MW GNA_{RE} by PGHPL, requirement of ICT augmentation at Jind(PG) is arising. Accordingly, it was proposed to grant 99 MW GNA_{RE} to PGHPL with augmentation of 1x500 MVA, 400/220 kV ICT(4th) at Jind(PG). Regarding the grant of GNA to Bulk Consumers, in Clause 12.5 of GNA Regulations, following is mentioned: <i>Quote</i> <i>"In case of an entity covered under Regulation 17.1(iii), the dedicated line to connect such an entity to the ISTS and necessary augmentation for providing connection to the ISTS, shall be constructed and maintained either by the entity itself or a licensee at the cost of such entity."</i> <i>Unquote</i>								

SI No.	Application No. & Date	Name of the Applicant	Nature of applicant	GNA _{RE} within Region (MW)	GNA _{RE} outside Region (MW)	Total GNA _{RE} Required (MW)	Start date of GNA _{RE}	End date of GNA _{RE}
Accordingly, as per the Clause 12.5 of GNA Regulations, the dedicated 220 kV D/c line to connect PGHPL to Jind(PG) S/s & augmentation of 1x500 MVA 400/220kV Jind ICT shall be constructed & maintained by PGHPL or by a ISTS licensee at the cost of PGHPL. Grid India in the meeting suggested to PGHPL that, since their load is just 99 MW, they may explore connectivity at intra state Jind(HVPN) S/s so that the cost implication of ICT augmentation at Jind(PG) can be avoided. Regarding this, PGHPL clarified that it is not feasible as intra state connectivity does not meet their assumptions considered during bidding of Green Hydrogen project. Therefore, they prefer connectivity at ISTS substation only. PGHPL informed that they need time to decide regarding connectivity at Jind S/s as they had not anticipated the requirement of additional 500 MVA ICT augmentation at Jind S/s under their scope. CTUIL informed that as PGHPL in their application as well as in meeting had indicated the requirement of connectivity at Jind S/s only, the same was considered and studies were carried out for grant by CTUIL. However, CTU suggested that PGHPL may also explore feasibility of connection at any other nearby ISTS substations like Sonipat, Kaithal etc. and inform the same to CTUIL in a week time. In the meantime, CTUIL will also carry out the studies for interconnection at Sonipat and Kaithal S/s as an alternative based on the availability of space & margin and will seek comments from CEA and Grid-India in this regard. PGHPL informed that they shall assess the same and inform CTUIL in a week time. Regarding this, CTUIL informed that there is no option to change the start date of GNA_{RE}. Therefore, PGHPL may inform their decision as early as possible so that the grant may be finalised in the next meeting. PGHPL agreed for the same. Accordingly, it was decided that the above application shall be deliberated again in the next CMETS NR meeting based on further communication from PGHPL .								

A4. Revision of Deemed GNA granted to Tanakpur HEP to 94.2 MW from earlier granted 94 MW

CTUIL informed that under clause 18.1(g) of GNA Regulations 2022 following is mentioned:

Quote

“The Central generating stations which are connected to the grid and have not been granted Long term Access under the Connectivity Regulations, 2009 but whose power is allocated by the Ministry of Power, shall be deemed to have been granted **GNA equal to the installed capacity** of such generating station(s).”

Unquote

As per clause 18.1(g), deemed GNA equal to the installed capacity were to be granted to central generation stations. In view of the above, after notification of GNA Regulations 2022, list of CGS entities along with the installed capacity & deemed GNA being granted to them were published in CTUIL website for observations & comments in October-2022 & April 2023. As per NRPC CGS allocation orders, installed capacity & deemed GNA granted to Tanakpur HEP was considered as 94 MW in the list published by CTUIL. Same was intimated to NHPC vide letter dated 31.10.2022.

Subsequently, based on the inputs received by various entities & Grid India, the list was again discussed with all stakeholders in 22nd CMETS NR meeting held on 21.08.2023.

No comments were received by CTUIL from NHPC regarding the installed capacity/Deemed GNA of Tanakpur HEP at any stage. Accordingly, based on the inputs and subsequent discussions held in 22nd CMETS NR meeting, the list of deemed GNA grantees was finalised and CTUIL vide letter dated 25.09.2023 granted Deemed GNA to all eligible entities.

However, recently, NHPC vide mail dated 11.09.2025 intimated that the Installed Capacity of Tanakpur Hydro Power Station is 94.2 MW (3x31.4 MW). Accordingly, NHPC requested to revise the Deemed GNA granted to Tanakpur HEP from 94 MW to 94.2 MW.

As per 18.1(g), deemed GNA is to be granted equal to the installed capacity of Central generating station. Accordingly, it matter regarding revision of IC and grant of corresponding deemed GNA to Tanakpur HEP for 94.2 MW was deliberated. NHPC, CEA, Grid India were asked to provide their observations regarding the same.

CEA informed that as per regulation the deemed GNA equal to the installed capacity is to be granted. Therefore, the same may be considered for revision in line with regulations. Grid India also agreed for the same. No comments were received in the meeting from stakeholders.

NHPC informed that, initially Tanakpur HEP had 3 units of installed capacity of 40 MW each(total 120 MW). Subsequently, in the year 1996 the installed capacity was derated to 3x31.4 MW (total derated installed capacity 94.2 MW). NHPC also informed that at the time of deemed GNA grant, it was assumed that the installed capacity was rounded off. Therefore, they did not provide any comments at that stage. The same round off figure of 94 MW is mentioned in NRPC allocation orders. In view of the above, NHPC requested to consider this minor correction to revise the deemed GNA to 94.2 MW from earlier granted 94 MW.

After deliberations it was decided to revise the deemed GNA granted to Tanakpur HEP to 94.2 MW.

Network Expansion scheme

1. Augmentation of 765/400 kV and 400/220 kV ICTs along with Implementation of 2 nos. of 220kV line bays & 1 no. of 400kV line at 765/400/220kV Ramgarh PS

In the meeting it was stated that 765/400/220kV Ramgarh PS is currently under implementation by M/s Ramgarh II Transmission Ltd {a subsidiary of Power Grid Corporation of India Ltd.} and is expected to be commissioned by Dec'25 as part of Transmission system for evacuation of power from REZ

in Rajasthan (20GW) under Phase-III Part C1. In this scheme, 2x1500 MVA 765/400 kV ICTs & 2x500 MVA 400/220 kV ICTs at Ramgarh PS are under implementation. At present total connectivity of 3984 MW have been granted at Ramgarh PS, out of which connectivity of about 3100MW (1200MW at 220kV level & 1900 MW at 400kV level) will be effective with Transmission system for evacuation of power from REZ in Rajasthan (20 GW) Phase III scheme. Out of 3100MW connectivity, 650MW capacity is granted on EHVAC scheme whereas 2450MW capacity is granted on HVDC scheme (Bhadla-Fatehpur). Balance 884 MW connectivity is associated with Ramgarh-II transmission scheme which is yet to be evolved.

It may be noted that the 1x1500 MVA ICT(3rd) at Ramgarh PS is already approved under Phase-II Part C2 scheme. However, the same was not taken up for implementation earlier due to non-receipt of applications. In view of above, to meet N-1 compliance and to enable immediate power evacuation, Augmentation of 765/400 kV, 1500 MVA (4th) ICT and 400/220 kV, 2x500 MVA (3rd & 4th) ICTs are required at Ramgarh PS. Further, 2 nos. of 220kV line bays (for M/s Migos Hybren Private Limited (600MW) & 1 no. of 400kV line bay (for M/s Adani Renewable Energy Holding Four Ltd (500+500MW)) at 765/400/220kV Ramgarh PS is also required in ISTS for RE connectivity.

In the meeting Grid-India enquired about the requirement of Augmentation of 765/400 kV, 1x1500 MVA (4th) ICT at Ramgarh PS with respect to connectivity quantum. CTU replied that total connectivity granted at Ramgarh PS 3984 MW. Out of this 3100 MW is granted with Ph-III Scheme. Therefore, considering total connectivity of about 4000 MW granted at Ramgarh PS, 4th ICT shall be required for power evacuation as well as to meet N-1 contingency. No comments were received in the meeting from stakeholders.

In view of above, following scheme was agreed to be implemented under ISTS:

Sl. No.	Description of Transmission Element	Scope of work (Type of Substation/Conductor capacity/km/no. of bays etc.)
1	Augmentation of 765/400 kV, 1x1500 MVA (4 th) ICT at 765/400kV Ramgarh PS	1500 MVA ICT- 1 no. 765 kV ICT Bay-1 no. 400 kV ICT Bay-1 no
2	Augmentation of 400/220 kV, 2x500 MVA (3 rd & 4 th) ICTs at 765/400kV Ramgarh PS	500 MVA ICT- 2 no. 400 kV ICT Bay-2 nos. 220 kV ICT Bay-2 nos.
3	Implementation of 2 nos. of 220kV line bays at 765/400kV Ramgarh PS	220 kV line bay - 2 nos.

4	Implementation of 1 no. of 400kV line bay at 765/400kV Ramgarh PS	400 kV line bay - 1 no.
---	---	-------------------------

2. Augmentation of 400/220 kV, 4x500 MVA (6th to 9th) ICTs along with 5 nos. of 220kV line bays and 1 no. of 400kV line bay at 765/400/220kV Bhadla-III PS

In the meeting it was stated that 765/400/220kV Bhadla-III PS is currently under implementation by POWERGRID Bhadla III Transmission Limited {a subsidiary of Power Grid Corporation of India Ltd.} with an implementation timeframe of Dec'25 as part of Transmission system for evacuation of power from REZ in Rajasthan (20GW) under Phase-III Part B1. At present total connectivity of 6500 MW have been granted at Bhadla-III PS (4050 MW at 220kV level & 2450MW at 400kV level). Out of 6500MW connectivity granted, 2990MW capacity is granted on EHVAC scheme (1990 MW at 220kV & 1000 MW at 400 kV) for which 4 nos. 765/400kV ICTs and 5 nos. 400/220kV ICTs are under implementation whereas 3510MW connectivity (2060 at 220 kV & 1450 at 400 kV) is granted on HVDC scheme (Bhadla – Fatehpur).

In view of above to enable immediate power evacuation and to meet N-1 compliance, Augmentation of 400/220 kV, 4x500 MVA (6th to 9th) ICTs are required in matching timeframe of HVDC scheme. Further, 5 nos. of 220kV line bays, 1 no. of 400kV line bay & 2 no. 400kV sectionalizer bay at 765/400/220kV Bhadla-III PS is also required in ISTS for RE connectivity. No comments were received in the meeting from stakeholders.

In view of above, following scheme was agreed to be implemented under ISTS:

Sl. No.	Description of Transmission Element	Scope of work (Type of Substation/Conductor capacity/km/no. of bays etc.)
1	Augmentation of 400/220 kV, 4x500 MVA (6 th to 9 th) ICTs at 765/400/220kV Bhadla-III PS	500 MVA CT- 4 nos. 400 kV ICT Bay-4 nos. 220 kV ICT Bay-4 nos.
2	Implementation of 5 nos. of 220kV line bays at 765/400/220kV Bhadla-III PS	220 kV line bay - 5 nos.
3	Implementation of 1 no. of 400kV line bay at 765/400/220kV Bhadla-III PS	400 kV line bay - 1 no.
4	Implementation of 2 no. 400kV sectionlizer bay at 765/400/220kV Bhadla-III PS	400kV sectionlizer bay-2 set

-----XXXXXXX-----

CENTRAL ELECTRICITY AUTHORITY
PLANNING WING
DATA MANAGEMENT & LOAD FORECASTING DIV.
ROOM NO. 715 (N) SEWA BHAWAN R.K. PURAM
NEW DELHI - 110 066

No. DMLE/PS/9/7/96-V01.IV/3530-85

Dt. 20th September, 1996.

NOTIFICATION FOR DERATION OF THE UNITS OF
THE TANAKPUR H.E PROJECT 3X40 MW - NHPC

NHPC had requested CEA for deration of their units at Tanakpur H.E Project from 40 MW each to 31.4 MW each due to change in pond level of the barrage from EL 248 m to EL 246.7 m for avoiding submergence of areas in Nepal and termination of tail race channel on upstream of Sarda Barrage where the maximum TWL was 223.3 m as against 220.385 m envisaged in the DPR for enabling Nepal to draw their requirement of water. Taking these two factors into account the maximum output possible from Tanakpur H.E is only 94.2 MW (3x31.4 MW) against installed capacity of 120 MW (3x40 MW) and the design energy is 460 MU instead of 525 MU. In appreciation of these constraints, derating of the Tanakpur H.E Machines as aforesaid is hereby accepted.

2. Accordingly, with effect from 1st September, 1996, the derated capacity and design potential of Tanakpur H.E. Project would be as follows :

Sl. No.	Installed Capacity & Design energy	Derated Capacity & Design energy.
1.	120 MW (3x40MW) & 525 MU	<u>94.2 MW (3x31.4MW)</u> & <u>460 MU</u>

This issues with the approval of Chairman, CEA,


Copy to :

1. Chairman, CEA
2. Member (HE)
3. Member (Planning)
4. Member (Power System)
5. Member (Grid Operation)
6. Member (Thermal)

CONTD....

Exhibit-I

Summer Solar Max Base case

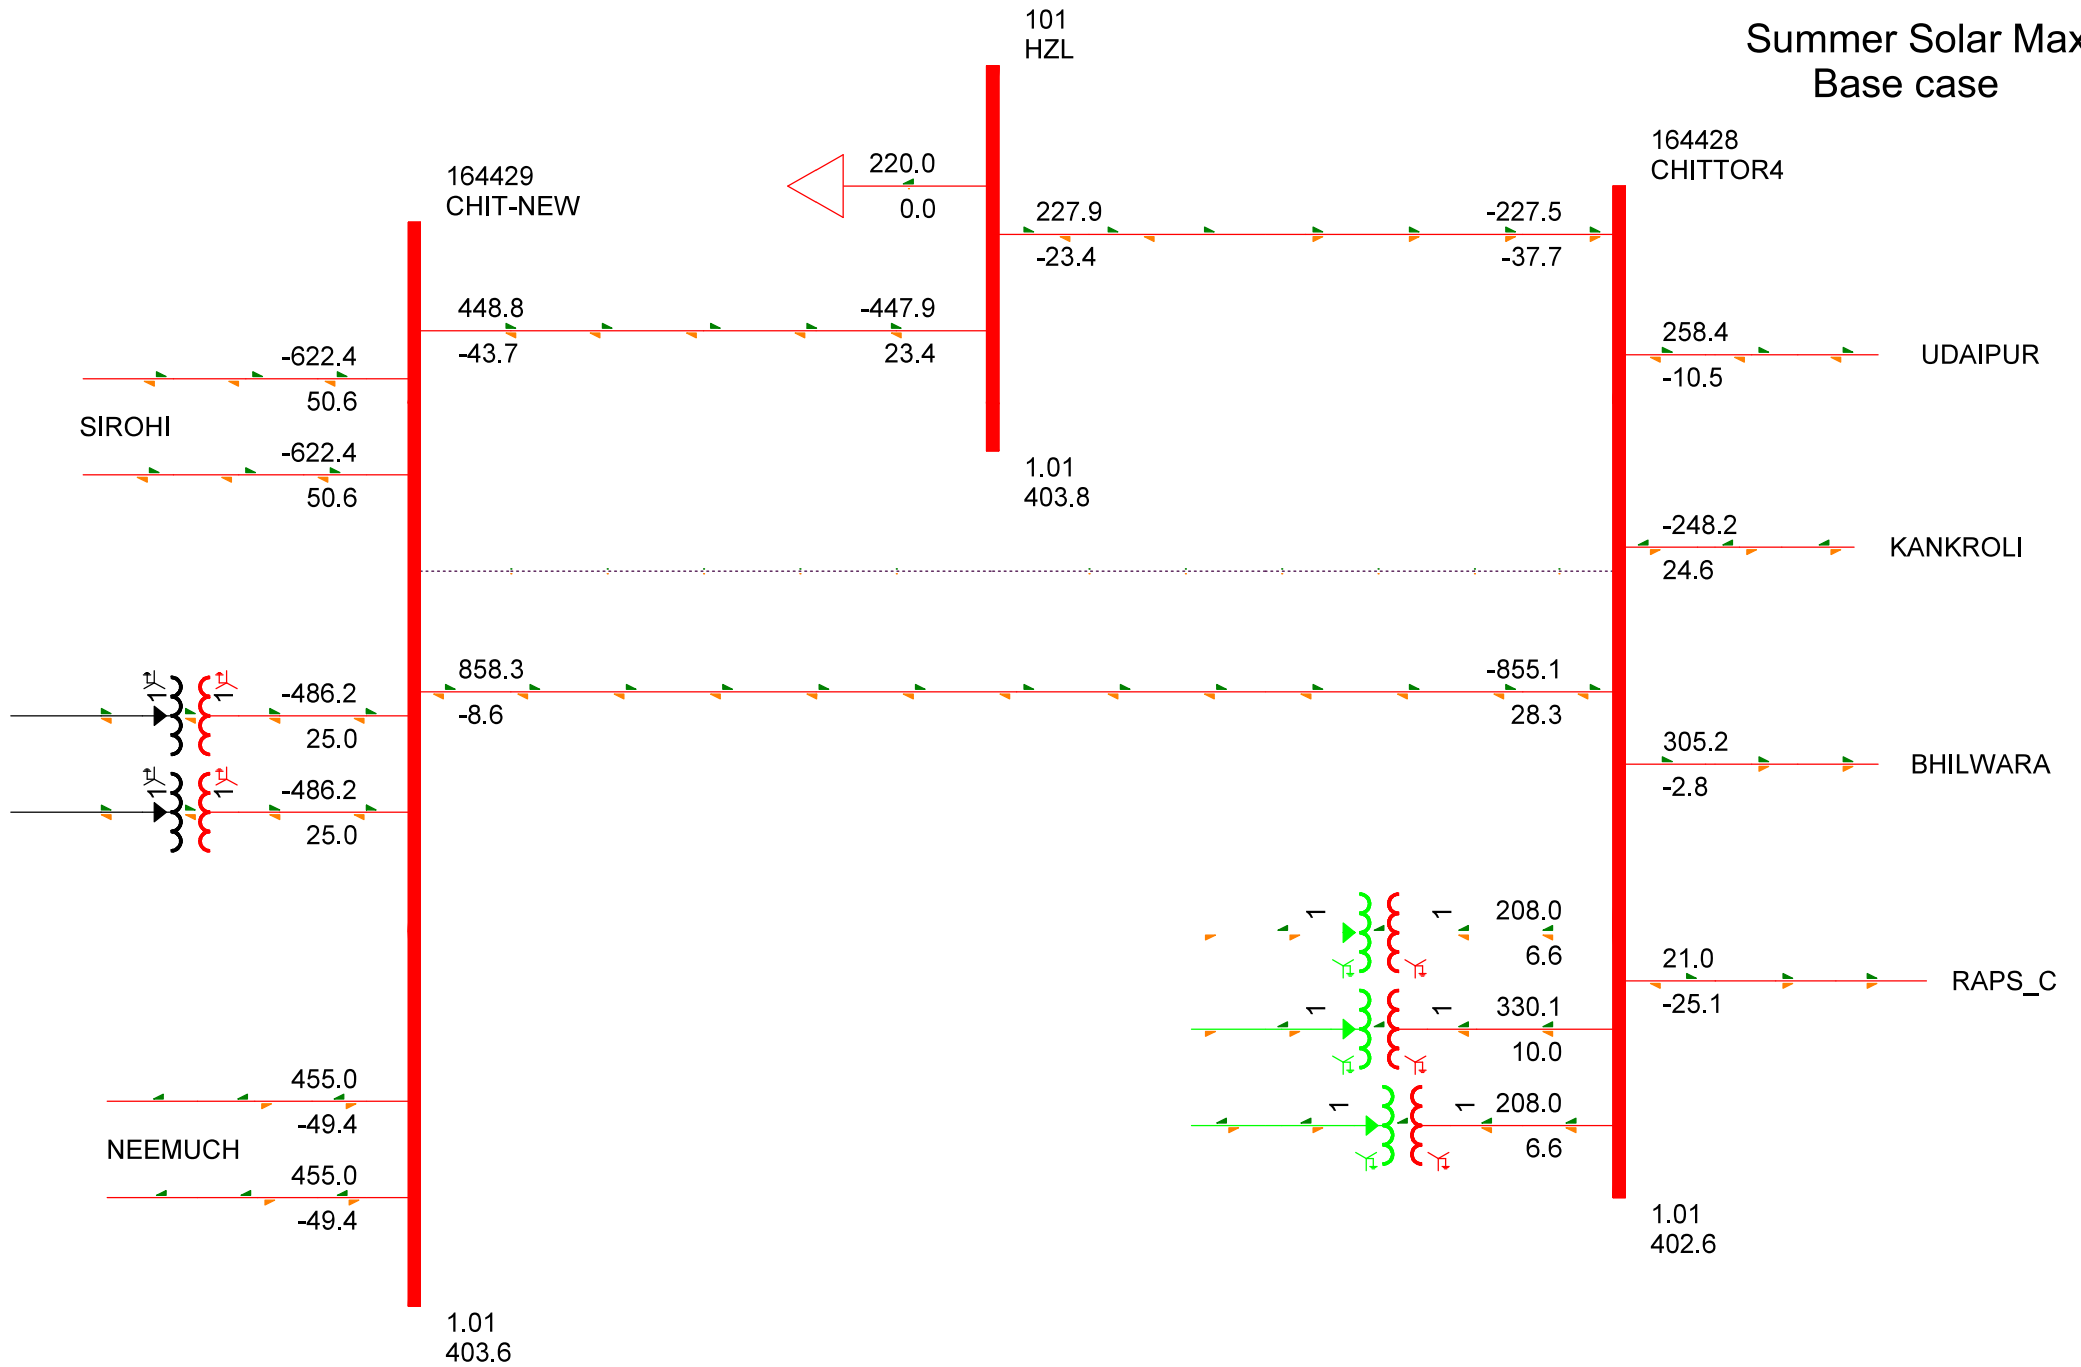

Winter Solar Max Base case

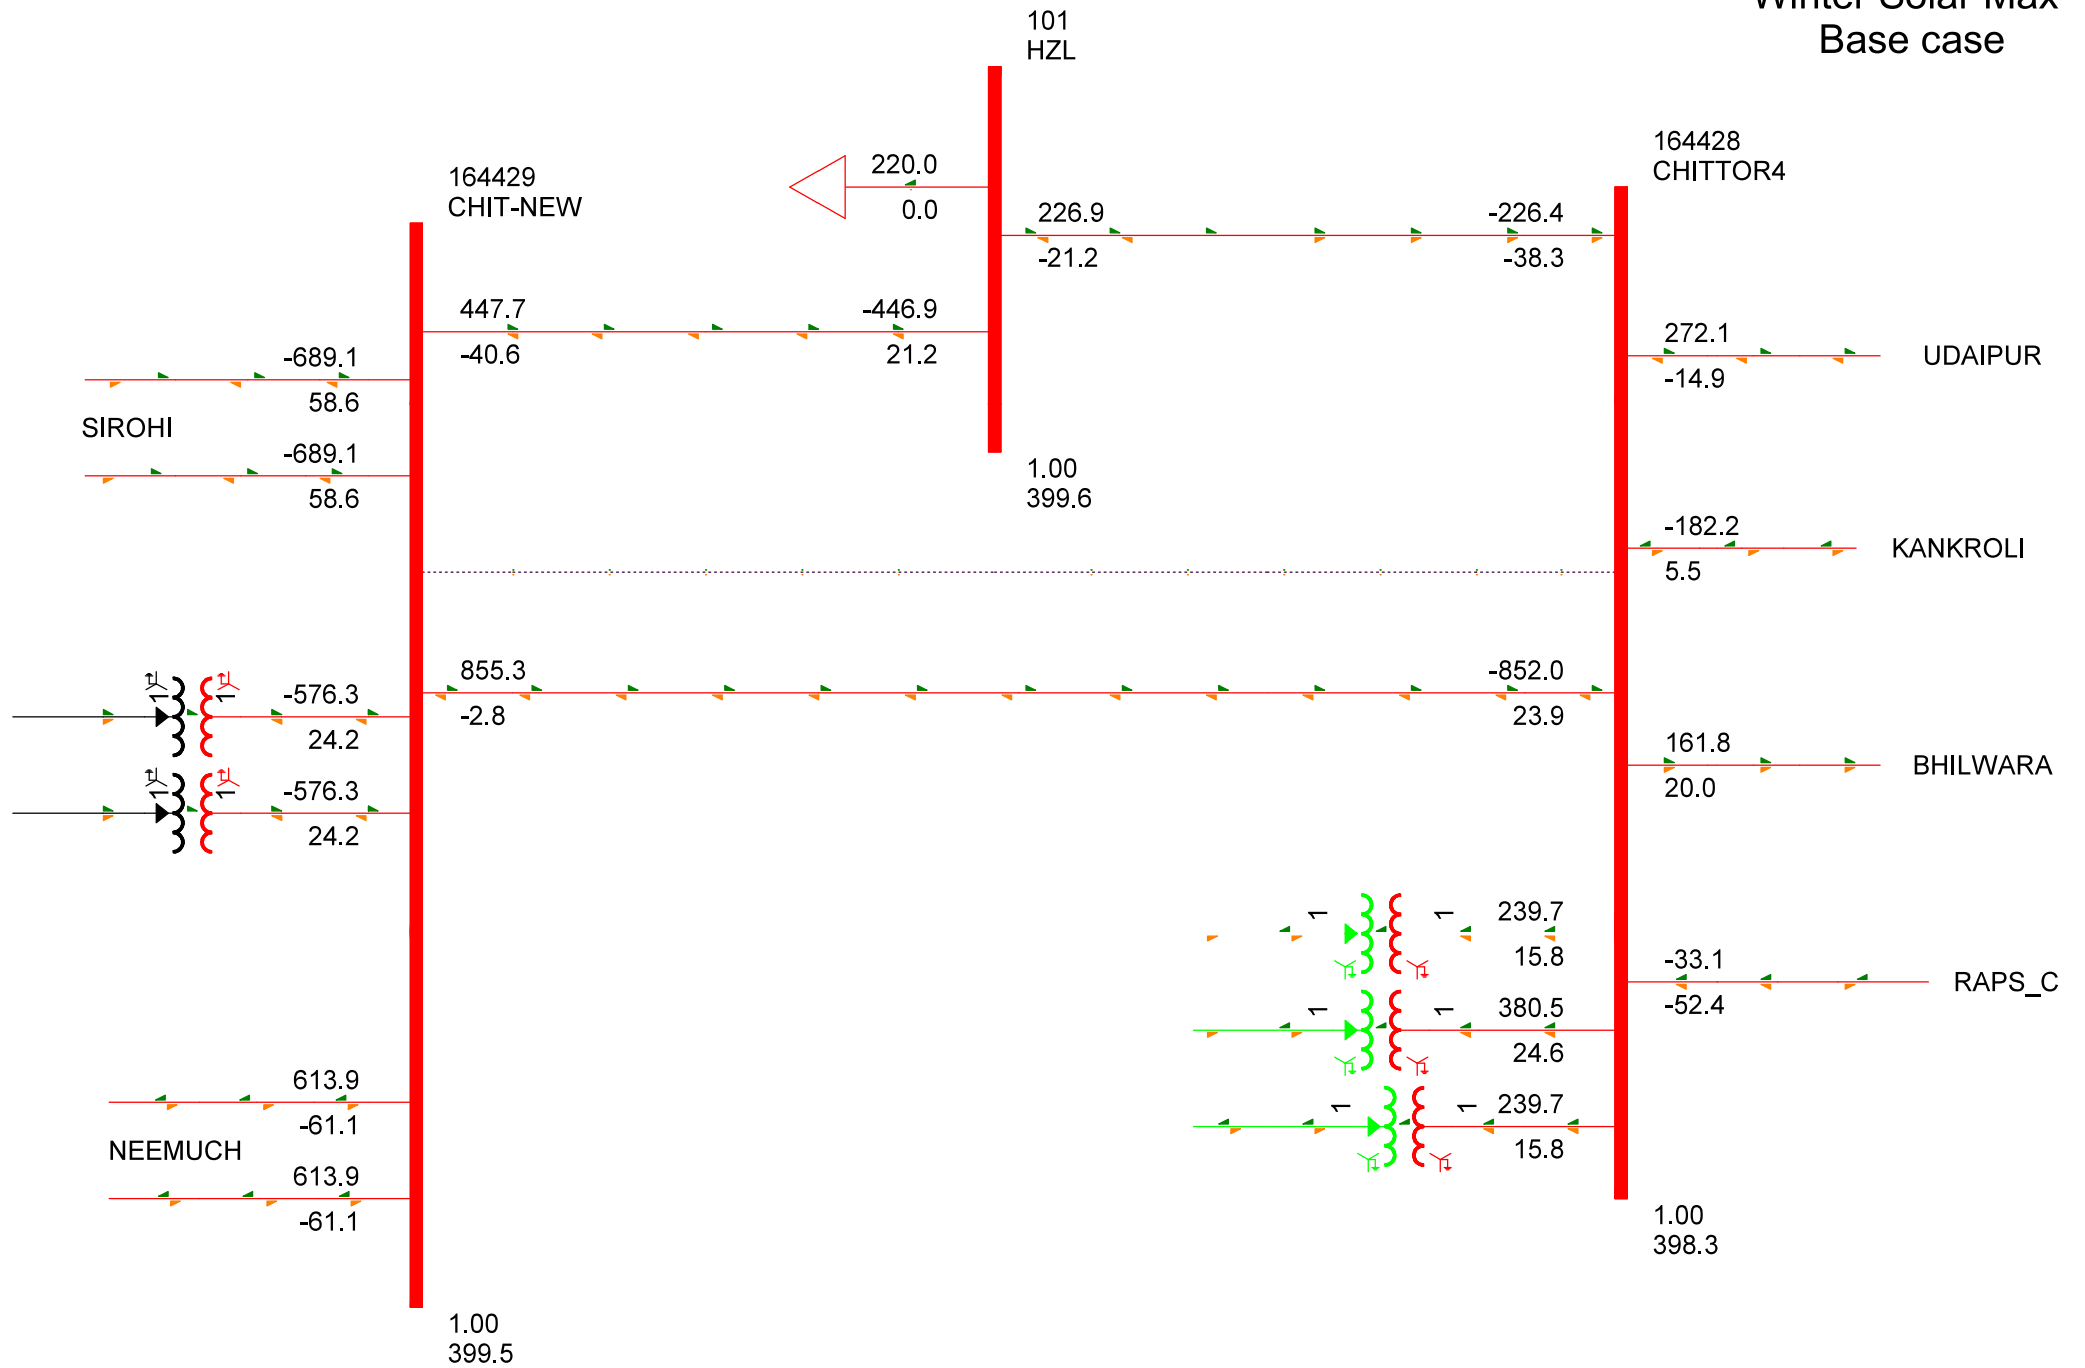


Exhibit-II

Summer Solar Max Base case


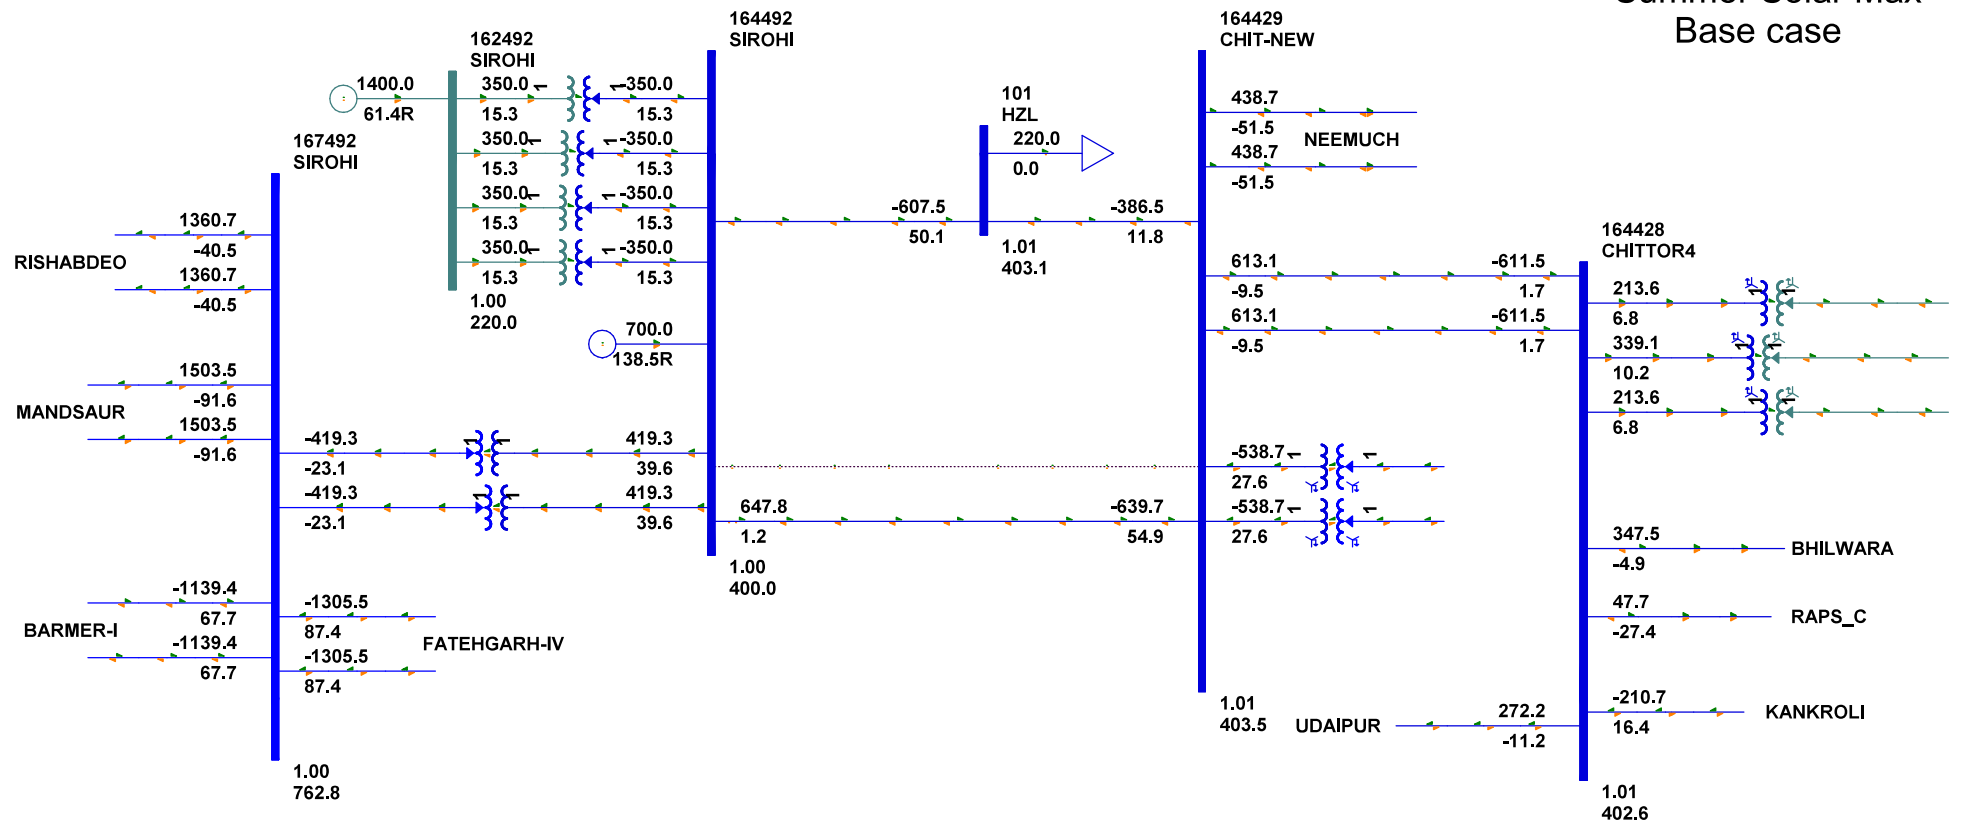


Exhibit-III

Summer Solar Max
Base Case

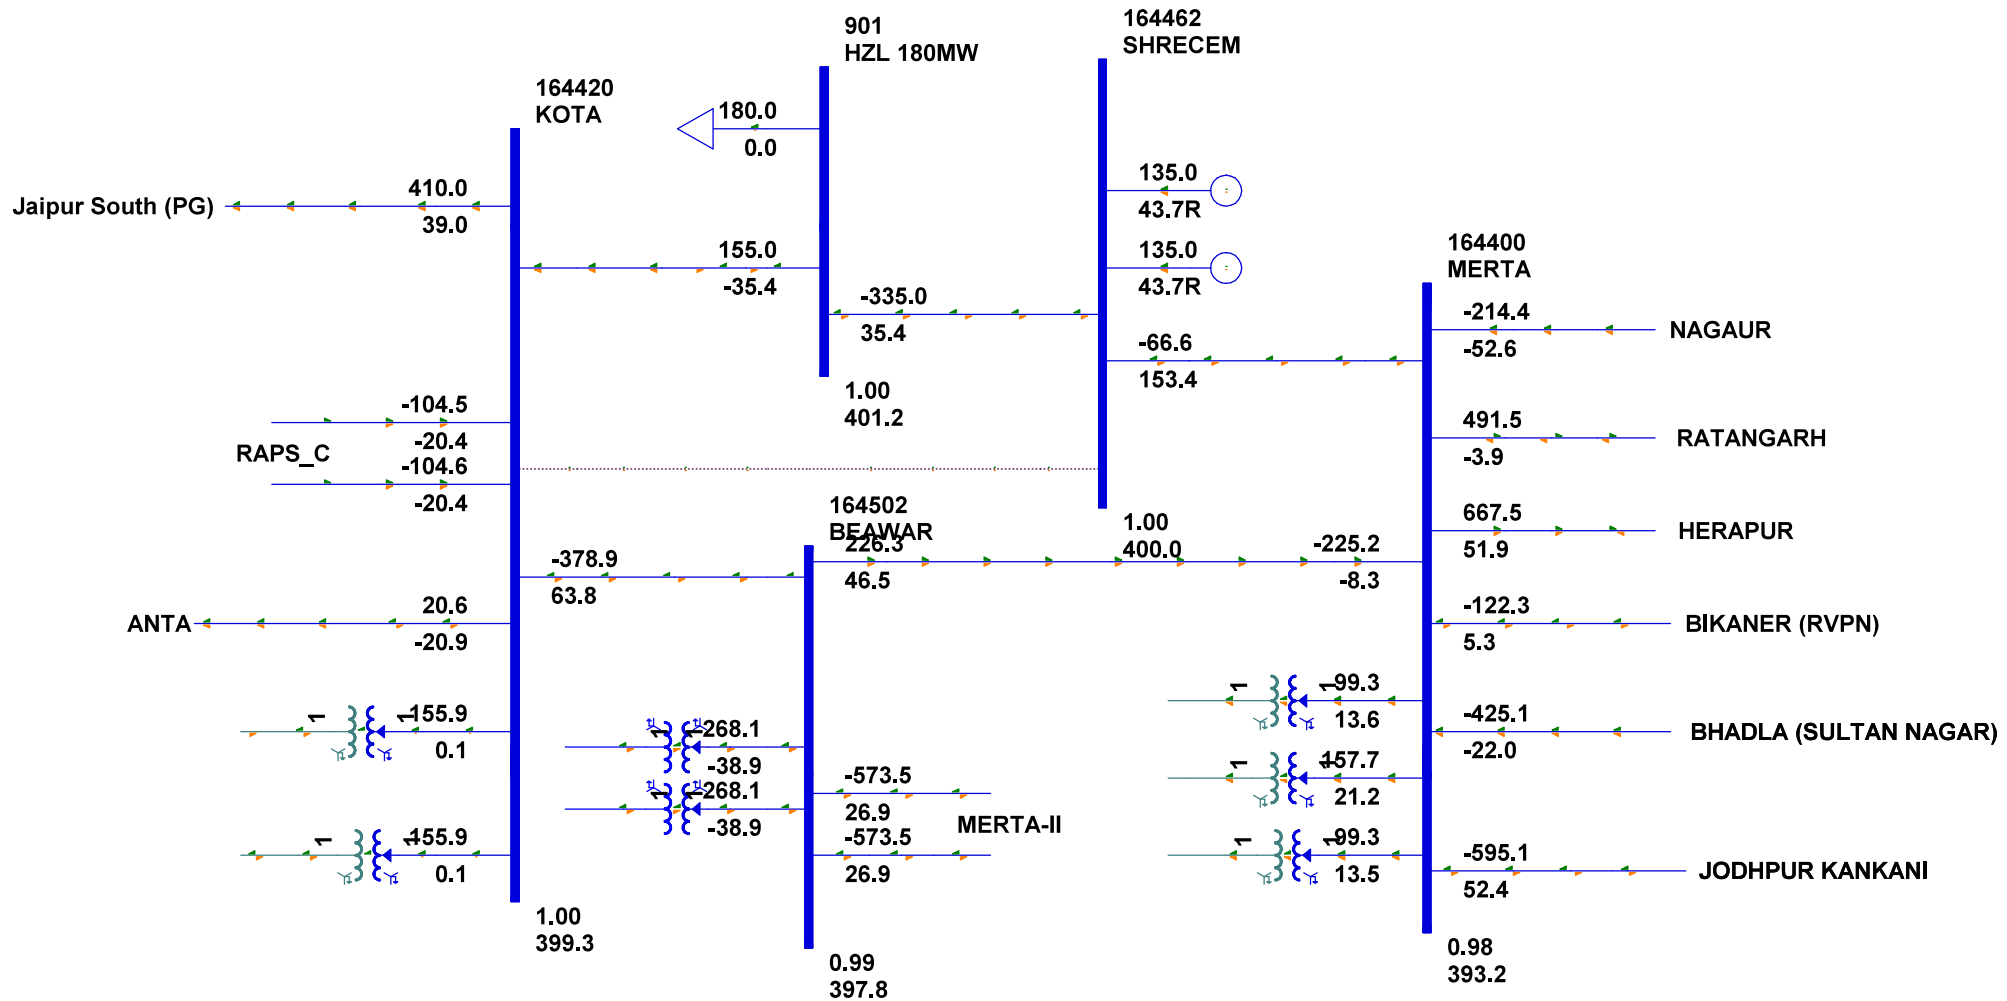

Winter Solar Max Base Case

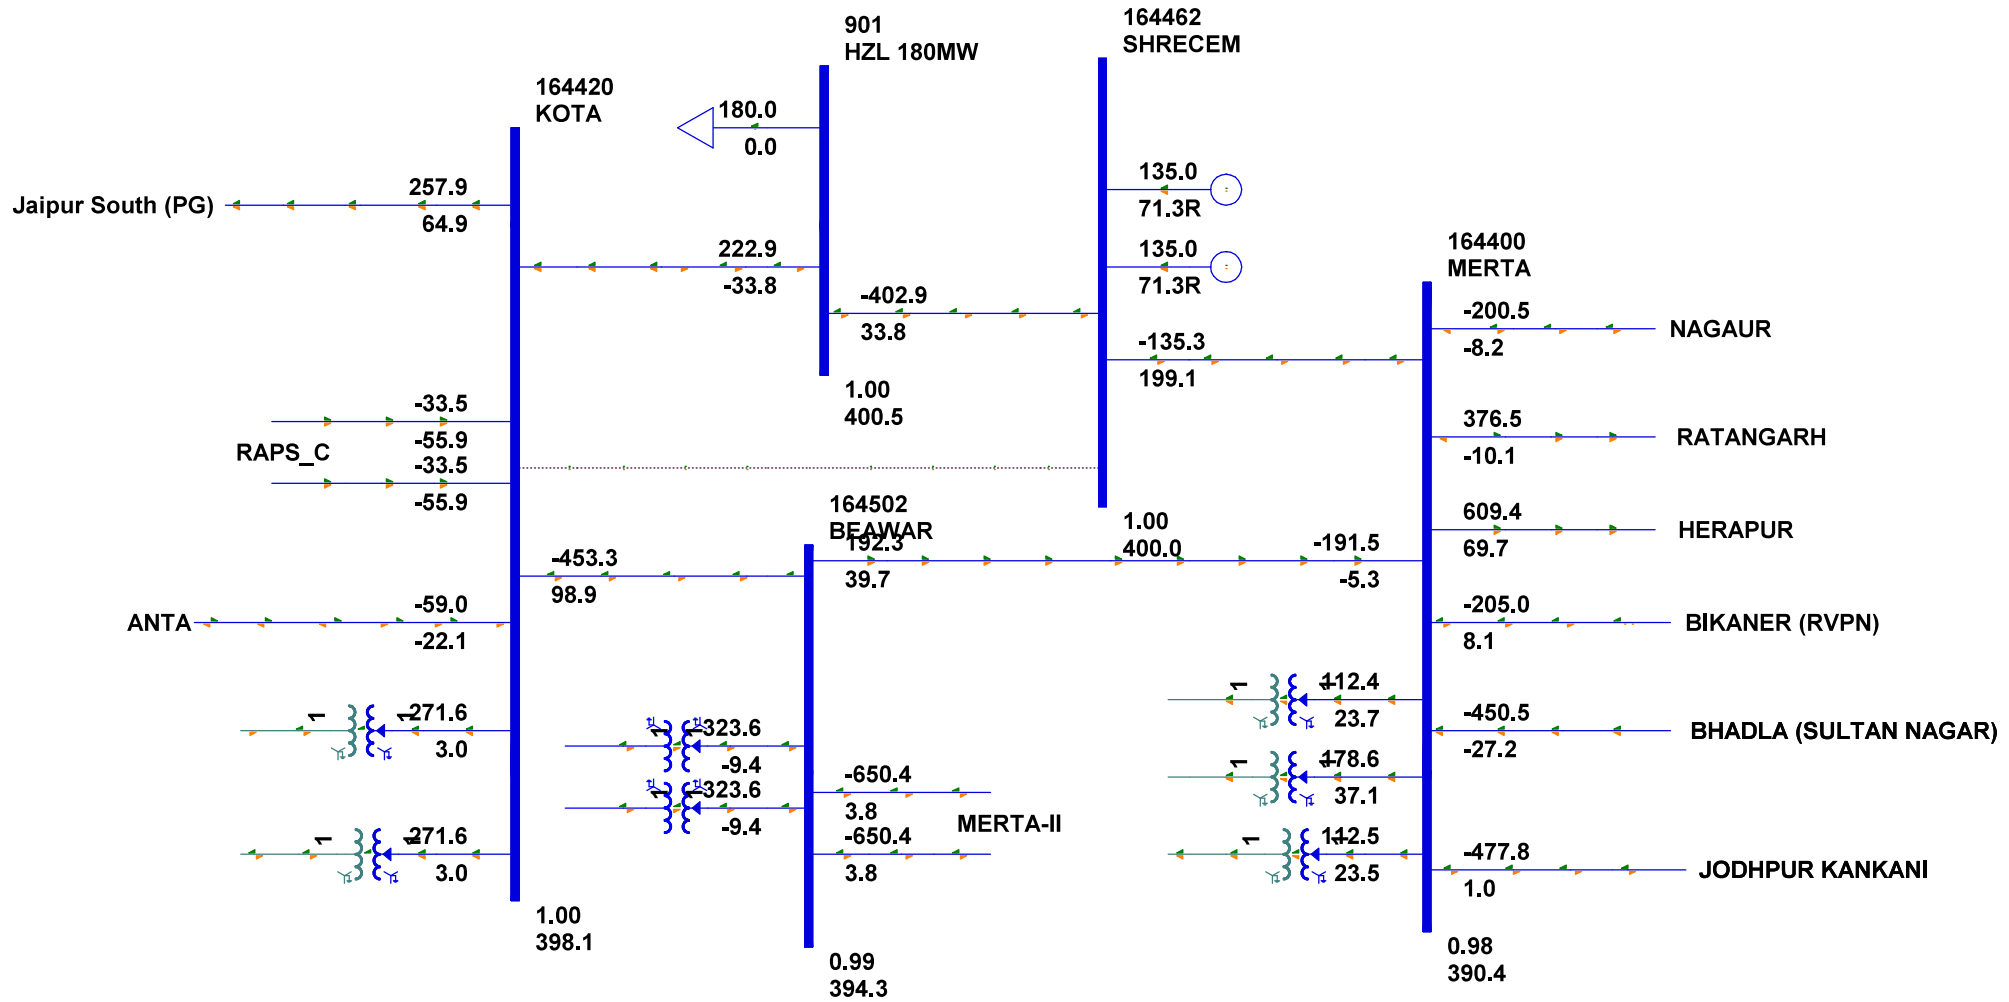


Exhibit-IV (PGHPL)

Summer Solar Max
Base Case

